

MONTHLY SITE UPDATE

Ladysmith Additions & Renovations



ACCOMPLISHMENTS

- Gym addition construction complete
- Auditorium soffit framed, drywalled, and painted
- Auditorium seat bottoms replaced
- Auditorium ceiling replaced
- Auditorium flooring complete
- Auditorium lobby paint complete
- Mechanical rooms boilers ordered

UPCOMING MONTH

- Complete construction in Auditorium
- Complete window shades in Media Center
- Install cafeteria courtyard pavilion
- Hang Ladysmith logos in building additions and main hall

BUDGET OVERVIEW

Total Project Cost = \$20,845,365
Remaining Contingency = \$55,000
Percent Complete = 92.00%



Completed construction in Media Center addition




Completed Gym Addition



Replaced Auditorium seat bottoms



Soffit above stage in Auditorium framed and drywalled

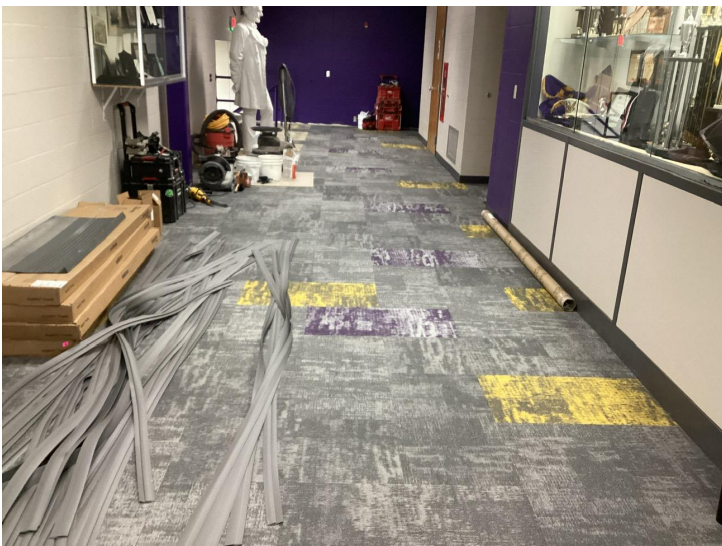

Carpet in Auditorium lobby being installed



Ceiling being replaced in Auditorium
