

MONTHLY SITE UPDATE

Ladysmith Additions & Renovations



ACCOMPLISHMENTS

- Media Center structural steel erected
- Framing and drywall is complete in Building 7
- Framing is complete in Building 4
- Cafeteria restrooms demolition complete
- Gym addition precast concrete erected
- Base coarse of new parking lot complete
- Drop off drive lane milled and excavated for base coarse
- Slab poured, grading and seeding in courtyard complete
- Football field lighting installed
- Continue electrical and mechanical demo and rough-ins
- Re-roofing continues
- Drain tile installation at exterior perimeter complete

UPCOMING MONTH

- Steel at new Gym addition to be installed
- Sheathing of wall at new Media Center addition
- Roofing at new Media Center addition
- Roofing at new Gym addition
- Continue electrical and mechanical demo and rough-ins
- Begin electrical and mechanical fixture installs
- Demo of hallway finishes, bathrooms, and locker rooms
- Fire sprinkler installation in Buildings 3, 4, and 7
- Paint, ceilings, flooring installed in Buildings 3, 4, and 7
- Flooring installation in Building 6
- Paving and striping of the new parking lot
- Football bleachers/press box to be replaced
- Re-roofing to continue at MS/HS

BUDGET OVERVIEW

Total Project Cost = \$20,845,365
Remaining Contingency = \$450,000
Percent Complete = 40.00%



Erecting Precast Concrete Panels for the New Gym




Demolition of Restrooms at Cafeteria



Grading Before Seeding in Large Courtyard



Finished Slab for Timber Canopy in Courtyard

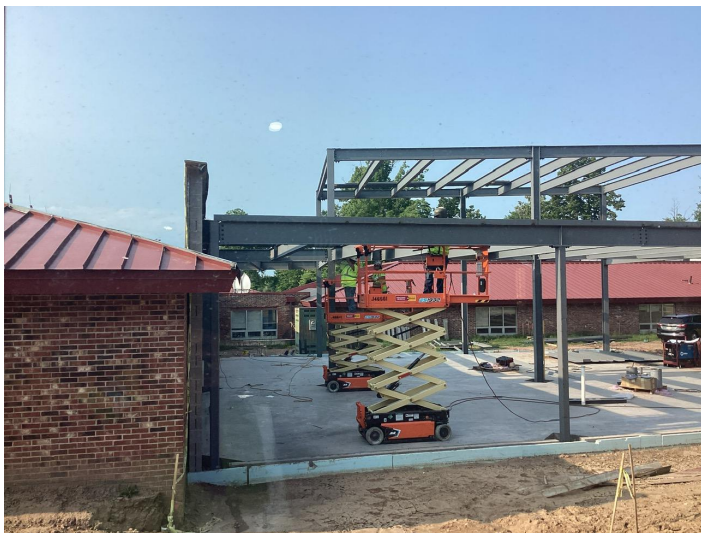

Structural Steel Erection for New Media Center



Drain Tile and Storm Water Pipe Leads for Roof Water Runoff
