

MONTHLY SITE UPDATE

Ladysmith Additions & Renovations



ACCOMPLISHMENTS

- Media Center exterior sheathing installed
- Renovated classrooms and hallways complete in Building 3
- Renovated classrooms and hallways complete in Building 7
- Renovated classrooms and hallways complete in Building 4
- Gym addition mechanical room is complete
- Retention Basin at parking lot is complete
- Renovated restrooms in buildings 2, 6, and cafeteria complete
- Science rooms 610 & 620 are complete
- Football field goal posts are installed
- Baseball and Softball Scoreboards are installed
- Electrical and mechanical finishes in existing spaces
- Roofing complete in building 3, gym and media center
- Grass seeding in miscellaneous areas as needed
- Fire Sprinkler system installed and certified by L.F.D.

UPCOMING MONTH

- Continue electrical and mechanical rough-ins
- Continue electrical and mechanical fixture installs
- Swap out roof top units for new equipment
- Grade, paving, and striping of south side parking lot
- Re-roofing and new roofing to continue at MS/HS
- Continue to hang doors at new additions
- Continue to install windows
- Pour slab for new gym floor and corridor
- Set steel decking on new gym corridor
- Install vapor barrier and exterior finish on media center
- Drywall media center interior walls
- Tuck-point and wash existing brick veneer
- Correct outstanding punch list items

BUDGET OVERVIEW

Total Project Cost = \$20,845,365
Remaining Contingency = \$275,000
Percent Complete = 70.00%



Sheathing Exterior Walls of Media Center




Block Walls and Foundations for Gym Corridor/Storage



New Floors and Vestibule Doorways



Installing Brick Veneer at Previous Gym/Cafeteria Connection

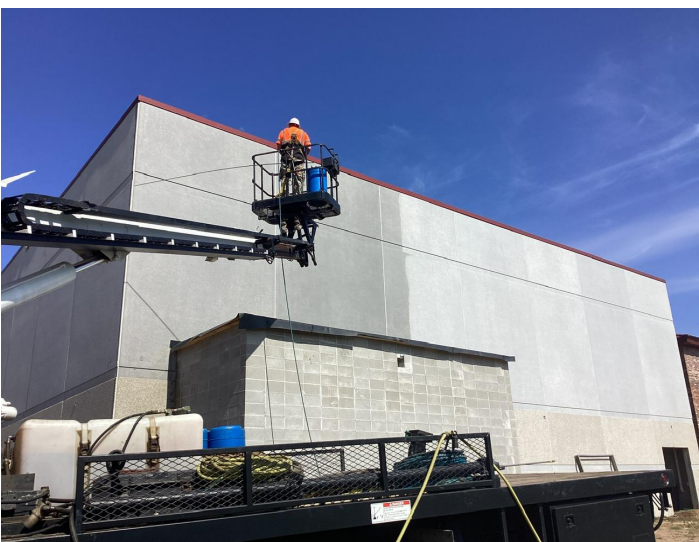

Concrete Panel Washing at Gym Addition



Renovated Classroom Space
